

LAB 2: AGILE BACKLOG CREATION & SPRINT SIMULATION IN JIRA

Academic Elective Bidding & Allocation System

Epic: Elective Allocation & Conflict Resolution

Name	Pallavi B
SRN	PES1UG24AM906
Project Key	AEBA
Tool	Jira - Company-managed Scrum

1. Epic, Backlog and User Stories

The selected Epic was **Elective Allocation & Conflict Resolution**. Six user stories were created to cover bid processing, ranked-preference allocation, timetable conflict checking, unresolved conflict handling, result finalization, and audit reporting.


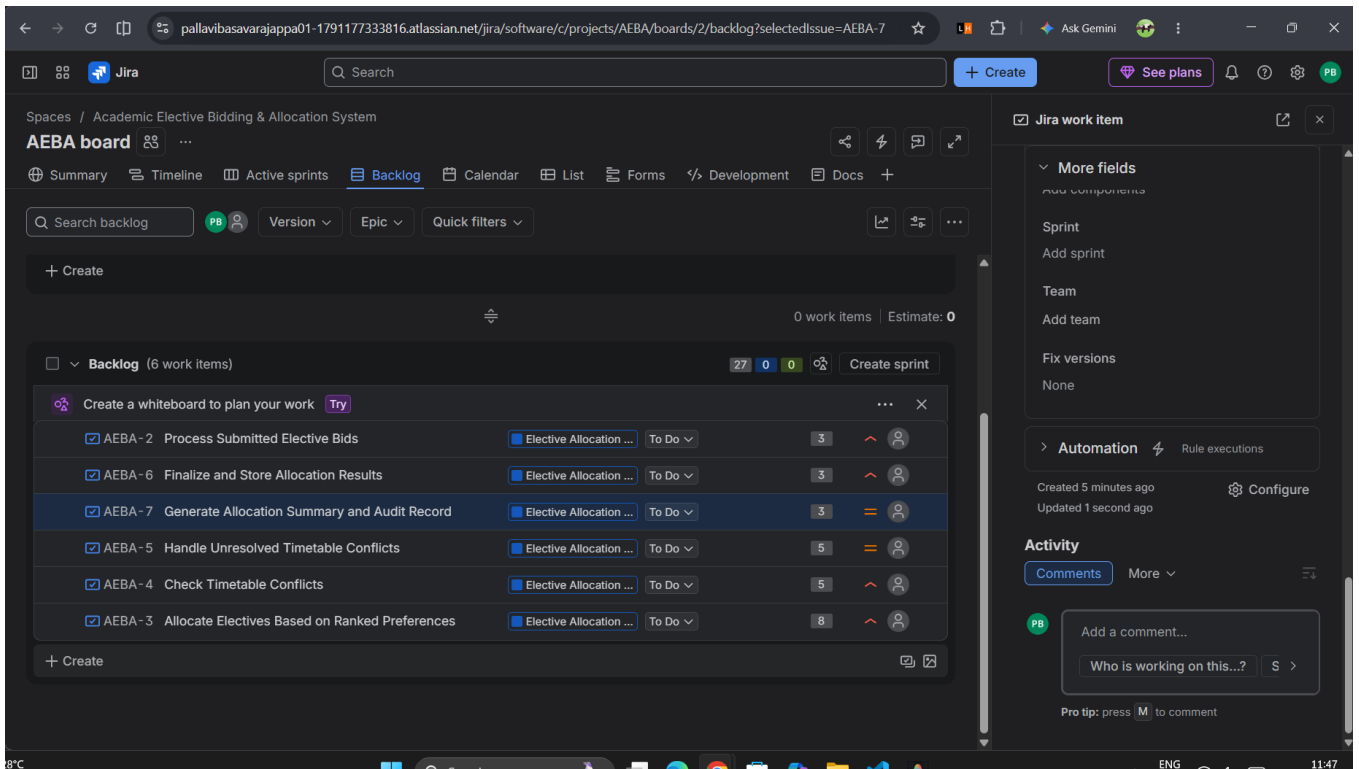


Figure 1. Initial Jira backlog containing all six user stories with a total estimate of 27 story points.

2. Final Epic and User Story Status

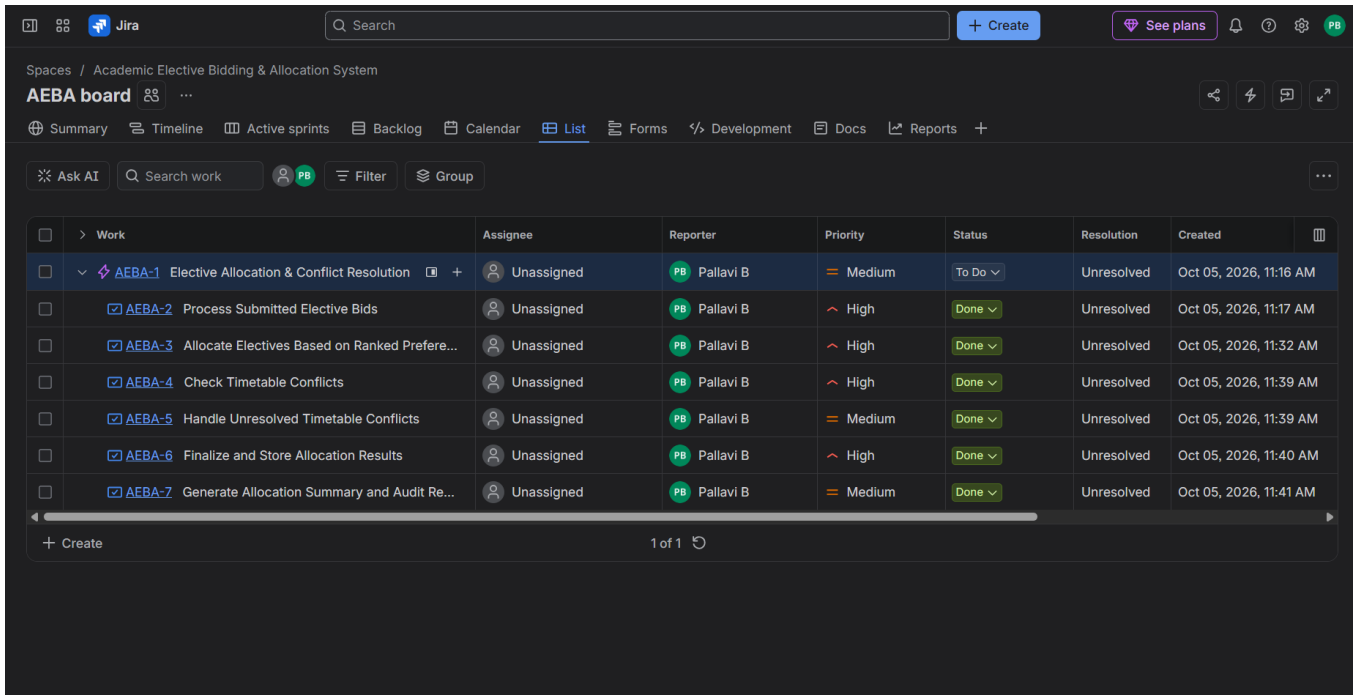

The screenshot displays the Jira interface for the 'AEBA board'. The top navigation bar includes the Jira logo, a search bar, a '+ Create' button, and a 'See plans' button. Below the navigation bar, the 'AEBA board' is selected, and the 'List' view is active. The main content area shows a table of work items. The first item is an Epic, 'AEBA-1 Elective Allocation & Conflict Resolution', which is expanded to show a list of seven user stories. Each user story has a checkbox, a title, an assignee (all are 'Unassigned'), a reporter (all are 'PB Pallavi B'), a priority, a status, a resolution, and a creation timestamp. The status of all user stories is 'Done', indicated by a green checkmark and a dropdown arrow. The resolution for all user stories is 'Unresolved'. The creation timestamps range from 'Oct 05, 2026, 11:16 AM' to 'Oct 05, 2026, 11:41 AM'. At the bottom of the table, there is a '+ Create' button and a '1 of 1' indicator.

☐	> Work	Assignee	Reporter	Priority	Status	Resolution	Created	
☐	▼ AEBA-1 Elective Allocation & Conflict Resolution +	Unassigned	PB Pallavi B	Medium	To Do	Unresolved	Oct 05, 2026, 11:16 AM	
☐	☑ AEBA-2 Process Submitted Elective Bids	Unassigned	PB Pallavi B	High	Done	Unresolved	Oct 05, 2026, 11:17 AM	
☐	☑ AEBA-3 Allocate Electives Based on Ranked Prefere...	Unassigned	PB Pallavi B	High	Done	Unresolved	Oct 05, 2026, 11:32 AM	
☐	☑ AEBA-4 Check Timetable Conflicts	Unassigned	PB Pallavi B	High	Done	Unresolved	Oct 05, 2026, 11:39 AM	
☐	☑ AEBA-5 Handle Unresolved Timetable Conflicts	Unassigned	PB Pallavi B	Medium	Done	Unresolved	Oct 05, 2026, 11:39 AM	
☐	☑ AEBA-6 Finalize and Store Allocation Results	Unassigned	PB Pallavi B	High	Done	Unresolved	Oct 05, 2026, 11:40 AM	
☐	☑ AEBA-7 Generate Allocation Summary and Audit Re...	Unassigned	PB Pallavi B	Medium	Done	Unresolved	Oct 05, 2026, 11:41 AM	

Figure 2. Jira List view showing AEBA-1 and user stories AEBA-2 to AEBA-7 with priorities and final Done status.

3. Priorities and Story Point Estimation

Story points were assigned using Fibonacci-style values according to relative complexity. The six stories total **27 story points**: 3, 8, 5, 5, 3 and 3.

Spaces / Academic Elective Bidding & Allocation System

AEBA board

Summary

Timeline

Active sprints

Backlog

Calendar

List

Forms

Development

Docs

Reports

Ask AI

Search work

PB

Filter

Group

	Reporter	Priority	Status	Resolution	Created	Updated	Due date	Story Points	
igned	PB Pallavi B	Medium	To Do	Unresolved	Oct 05, 2026, 11:16 AM	Oct 05, 2026, 11:16 AM	None	None	
igned	PB Pallavi B	High	Done	Unresolved	Oct 05, 2026, 11:17 AM	Oct 05, 2026, 4:19 PM	None	3	
igned	PB Pallavi B	High	Done	Unresolved	Oct 05, 2026, 11:32 AM	Oct 05, 2026, 4:20 PM	None	8	
igned	PB Pallavi B	High	Done	Unresolved	Oct 05, 2026, 11:39 AM	Oct 05, 2026, 4:21 PM	None	5	
igned	PB Pallavi B	Medium	Done	Unresolved	Oct 05, 2026, 11:39 AM	Oct 05, 2026, 4:52 PM	None	5	
igned	PB Pallavi B	High	Done	Unresolved	Oct 05, 2026, 11:40 AM	Oct 05, 2026, 4:53 PM	None	3	
igned	PB Pallavi B	Medium	Done	Unresolved	Oct 05, 2026, 11:41 AM	Oct 05, 2026, 4:53 PM	None	3	

+ Create

1 of 1

Figure 3. Jira List view showing Priority, Status and Story Points.

4. Sprint 1 - Core Allocation Workflow

Sprint Goal: Complete the core elective allocation workflow by processing submitted bids, allocating electives based on ranked preferences, and identifying timetable conflicts.

Stories: AEBA-2 (3 SP), AEBA-3 (8 SP), AEBA-4 (5 SP). **Total: 16 SP.**

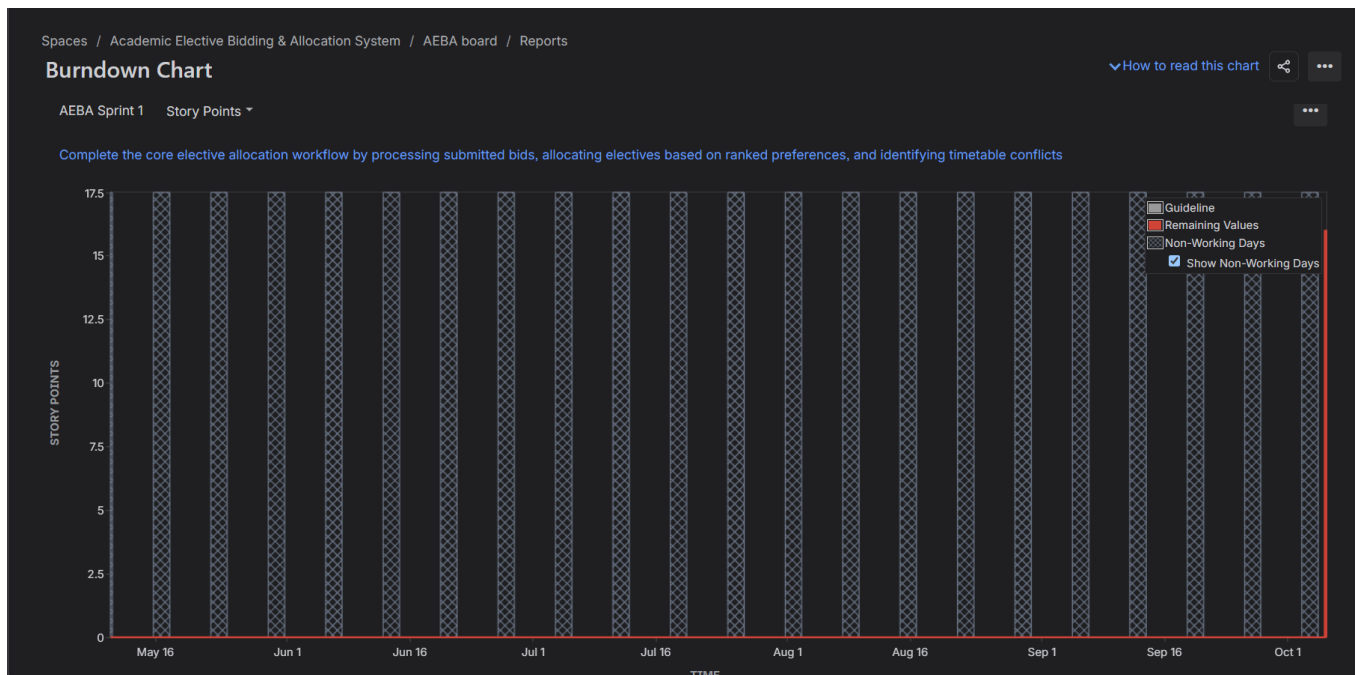


Figure 4. Sprint 1 Burndown Chart.

5. Sprint 1 Burndown Event Details

The event table records the Sprint 1 scope changes and the simulated completion of the three stories. Remaining work decreased from **16 to 13 to 5 to 0 story points**.

Date	Issue	Event Type	Event Detail	Story Points		
				Inc.	Dec.	Remaining
10/May/26 12:19 PM	Total	Sprint start				0
05/Oct/26 11:50 AM	AEBA-2	Scope change	Issue added to sprint	3		3
	AEBA-3	Scope change	Issue added to sprint	8		11
	AEBA-4	Scope change	Issue added to sprint	5		16
05/Oct/26 4:19 PM	AEBA-2	Burndown	Issue completed		3	13
05/Oct/26 4:20 PM	AEBA-3	Burndown	Issue completed		8	5
05/Oct/26 4:21 PM	AEBA-4	Burndown	Issue completed		5	0
05/Oct/26 4:24 PM	AEBA-2	Sprint ended by Pallavi B				0
	AEBA-3					0
	AEBA-4					0
	Total					0

Figure 5. Sprint 1 burndown event details showing AEBA-2, AEBA-3 and AEBA-4 completed.

6. Sprint 1 Sprint Report



Figure 6. Sprint 1 Sprint Report and chart.

Status Report						* Issue added to sprint after start time
Completed Issues						View in Issue Navigator
Key	Summary	Issue Type	Priority	Status	Story Points (16)	
AEBA-2 *	Process Submitted Elective Bids	☒ Story	High	DONE	3	
AEBA-3 *	Allocate Electives Based on Ranked Preferences	☒ Story	High	DONE	8	
AEBA-4 *	Check Timetable Conflicts	☒ Story	High	DONE	5	

Figure 7. Sprint 1 Status Report showing all three stories completed for 16 story points.

7. Sprint 2 - Conflict Resolution and Finalization

Sprint Goal: Complete the remaining elective allocation workflow by handling unresolved timetable conflicts, finalizing allocation results, and generating the allocation summary and audit record.

Stories: AEBA-5 (5 SP), AEBA-6 (3 SP), AEBA-7 (3 SP). **Total: 11 SP.**

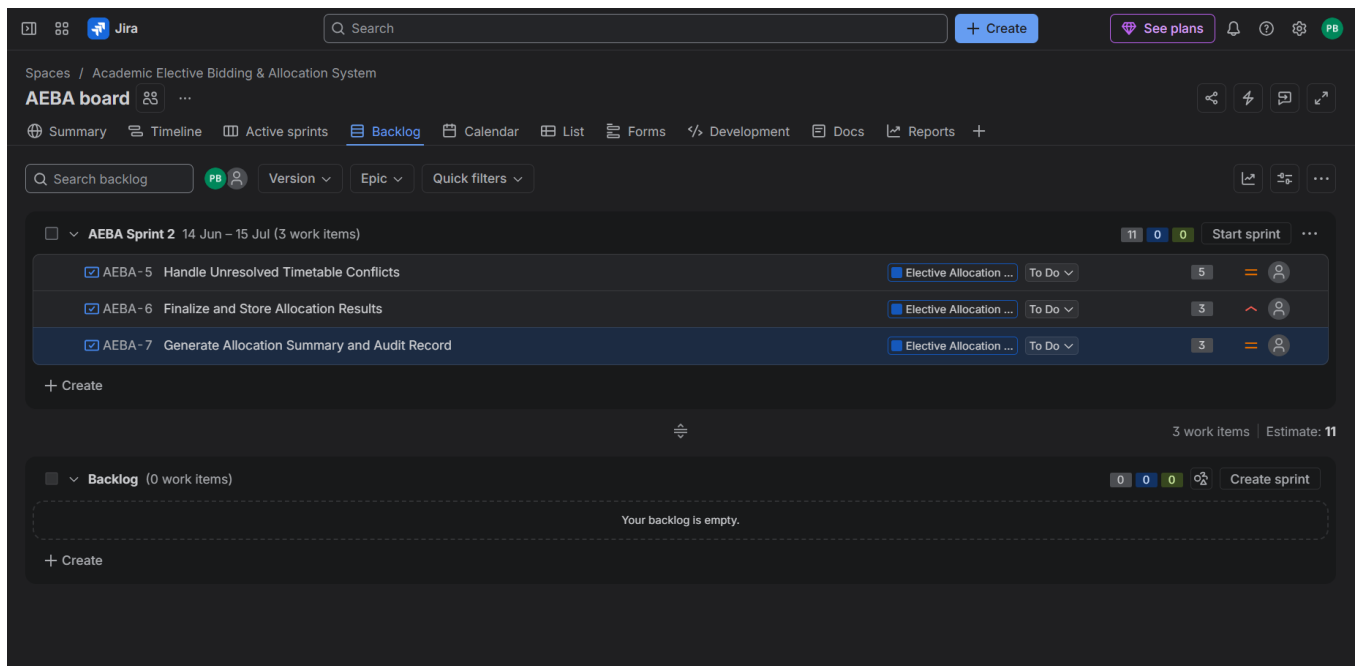


Figure 8. Sprint 2 backlog containing the three remaining user stories with an estimate of 11 story points.

8. Sprint 2 Burndown Chart

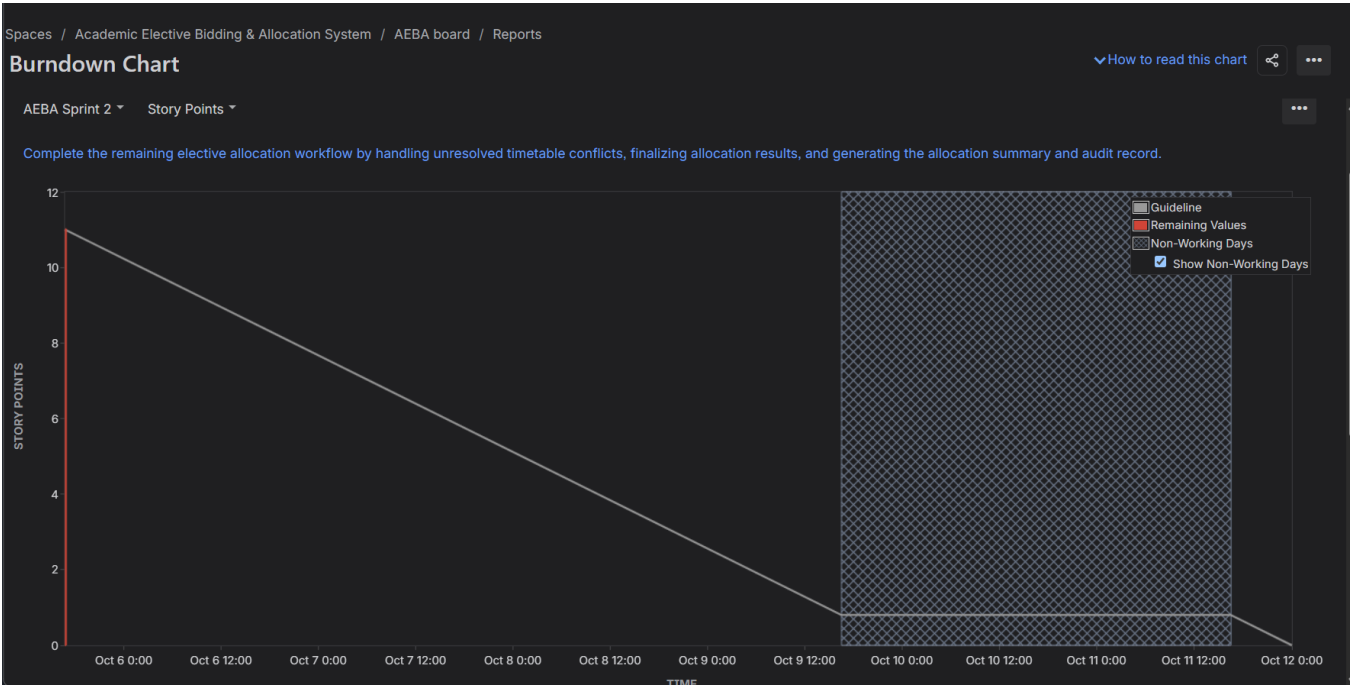


Figure 9. Sprint 2 Burndown Chart for the 11 committed story points.

9. Sprint 2 Burndown Event Details

The Sprint 2 event table shows remaining work decreasing from **11 to 6 to 3 to 0 story points**.

Date	Issue	Event Type	Event Detail	Story Points		
				Inc.	Dec.	Remaining
05/Oct/26 4:48 PM	AEBA-5	Sprint start		5		
	AEBA-6			3		
	AEBA-7			3		
	Total					11
05/Oct/26 4:52 PM	AEBA-5	Burndown	Issue completed		5	6
05/Oct/26 4:53 PM	AEBA-6	Burndown	Issue completed		3	3
	AEBA-7	Burndown	Issue completed		3	0
05/Oct/26 4:54 PM	AEBA-5	Sprint ended by Pallavi B				0
	AEBA-6					0
	AEBA-7					0
	Total					0

Figure 10. Sprint 2 burndown event details.

10. Sprint 2 Sprint Report

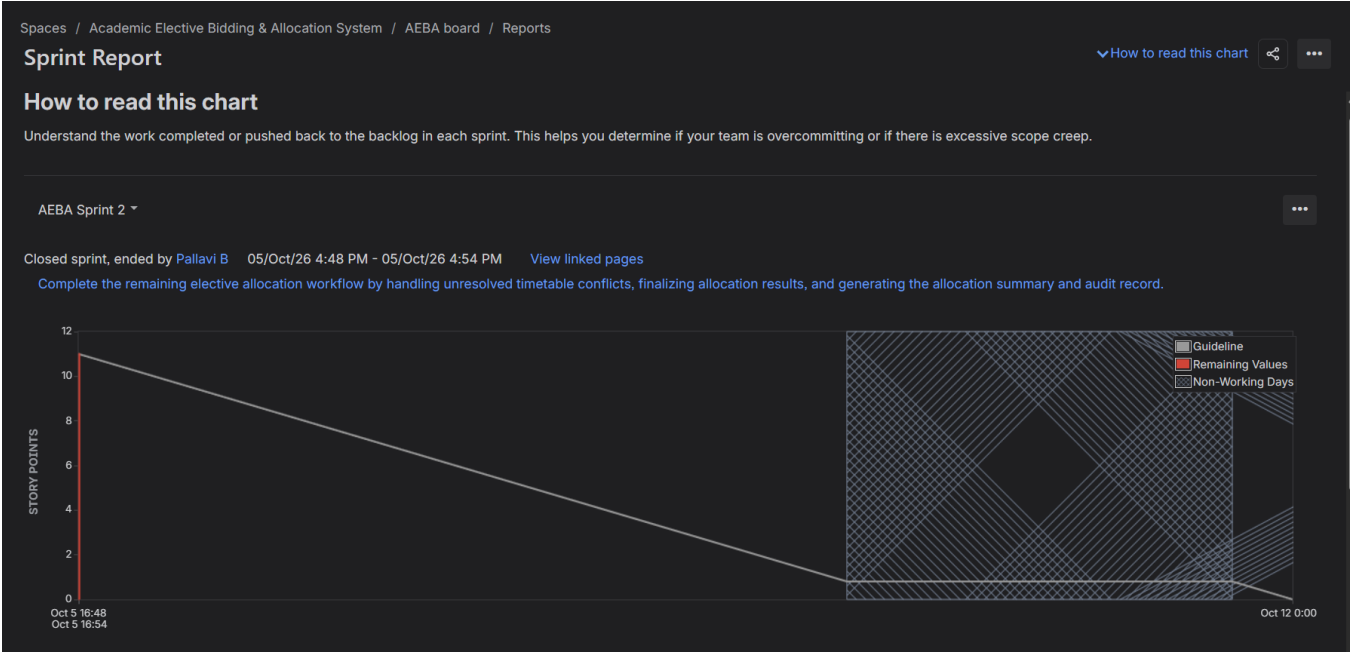


Figure 11. Sprint 2 Sprint Report showing the closed sprint and sprint goal.

Status Report

Completed Issues

[View in Issue Navigator](#)

Key	Summary	Issue Type	Priority	Status	Story Points (11)
AEBA-5	Handle Unresolved Timetable Conflicts	☒ Story	Medium	DONE	5
AEBA-6	Finalize and Store Allocation Results	☒ Story	High	DONE	3
AEBA-7	Generate Allocation Summary and Audit Record	☒ Story	Medium	DONE	3

Figure 12. Sprint 2 Status Report showing AEBA-5, AEBA-6 and AEBA-7 completed for 11 story points.

11. Reflection Questions

1. Did your estimations reflect the actual effort?

Yes. The story-point estimations reflected the relative complexity of the user stories. More complex activities such as allocating electives based on ranked preferences were assigned higher story points, while simpler activities such as storing results and generating the allocation summary were assigned fewer points. Sprint 1 contained 16 story points, while Sprint 2 contained 11 story points. Since this was a simulated sprint, the points represent estimated effort rather than actual development time.

2. Was your backlog well-prioritized?

Yes. The backlog was prioritized according to the importance of each activity in the elective allocation workflow. Core functions such as processing submitted bids, allocating electives, checking timetable conflicts, and finalizing allocation results were given High priority. Supporting activities such as handling unresolved conflicts and generating the audit record were assigned Medium priority.

3. How did your simulated sprint align with your plan?

The simulated sprints aligned with the planned workflow. Sprint 1 completed the three core stories for 16 story points. Sprint 2 completed the remaining three stories for 11 story points. All six planned user stories were completed.

4. What insights did the burndown chart give about your team's capacity?

The burndown evidence shows that all committed story points were completed. In Sprint 1, the remaining work decreased from 16 to 13, then 5, and finally 0 story points. In Sprint 2, it decreased from 11 to 6, then 3, and finally 0. Because this was a lab simulation and the workflow states were updated within a short period, the burn occurred much faster than it would in a real development sprint. The charts nevertheless demonstrate how Jira tracks remaining work and sprint completion.

Conclusion

The Jira simulation successfully converted the requirements of the Academic Elective Bidding & Allocation System into an Agile backlog, prioritized and estimated the user stories, and completed the planned work across two sprints. The exercise demonstrated backlog management, sprint planning, workflow tracking, burndown analysis, and sprint reporting.
